

PROJECT STATUS UPDATE

Farmington Public Schools

Bid Package # 16

2020 Bond Issue - Visions Unlimited



Visions Unlimited – Project Description

Project Description:


The Visions Unlimited project includes demolition and re-work throughout the interior and exterior of the old Farmington Central High School building in order to provide a new space for the Visions Unlimited program.



Visions Unlimited – Project Overview

Project Overview:

Gypsum board continues to be installed, taped and mudded throughout the building.

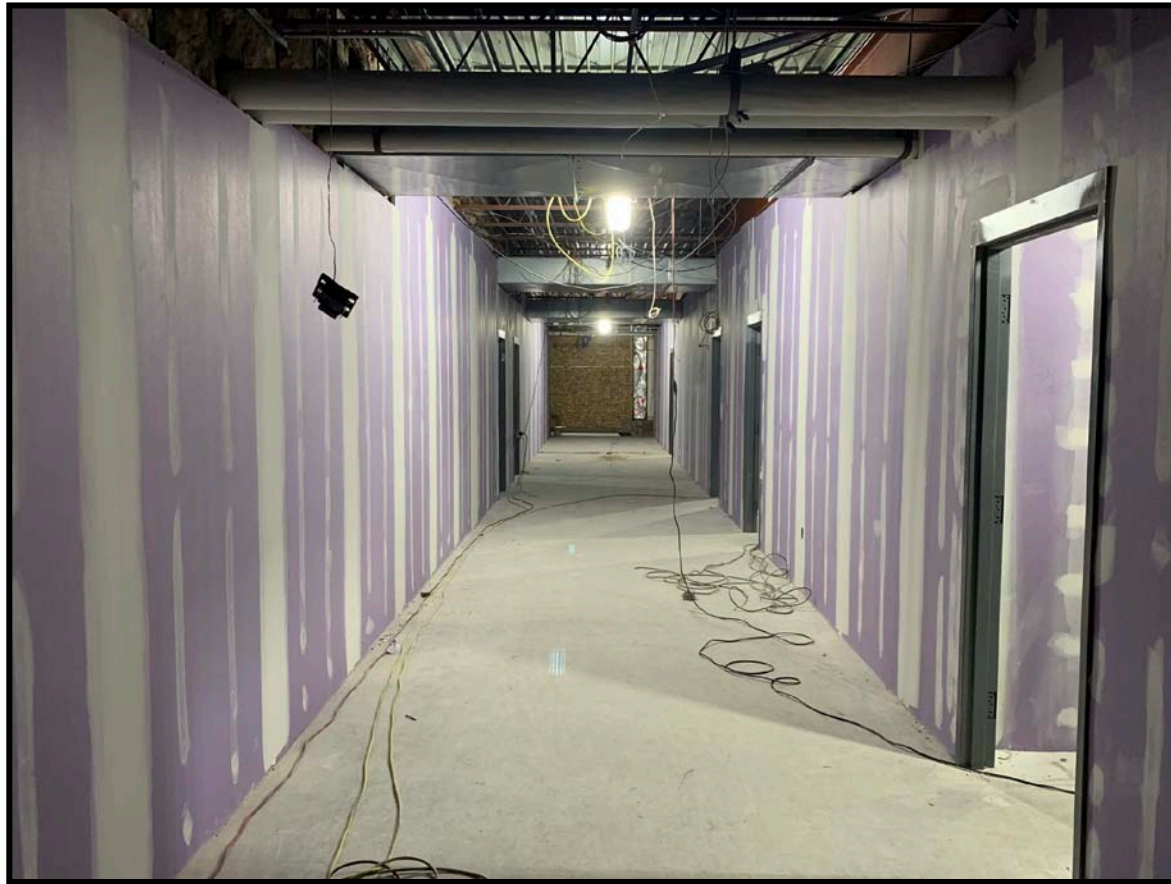

Visions Unlimited – Project Overview

Project Overview:

Existing casework that was to be re-used has been re-installed in selective classrooms. Field measuring for new countertops to follow.



Visions Unlimited – Project Overview

Project Overview:




Masonry infills around new door frames is ongoing.



New fire suppression piping is currently being installed.

Visions Unlimited – Three Week Look Ahead

		FPS 2021 Bid Pack 16: Visions Unlimited																				Period Start: 2/20/2023			
		3-WEEK LOOK-AHEAD SCHEDULE																				Period End: 3/12/2023			
																						Prepared By: Jeff Robinette			
																						Page: 1 of 1			
Activity Description	Contractor	Scheduled Start	Week 1 2/20/2023							Week 2 2/27/2023							Week 3 3/6/2023							Scheduled Finish	Remarks
			20	21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11	12		
			M	T	W	Th	F	S	S	M	T	W	Th	F	S	S	M	T	W	Th	F	S	S		
Visions Unlimited																									
Electrcal Rough	Max Elec	12/27/23	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			2/24/23	Bulletin needed for new panel location
Interior Masonry	Navetta Mason	12/12/22								X	X	X	X	X										2/17/23	Plumbing issues need to be resolved to complete
Drywall Install	AM Higley	1/30/23	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			3/3/23	
UG/Rough Plumbing	Contrast Mech																								Not scheduled. Need RFI answers to continue.
Cabinet Re-Installation	Wally K	2/20/23	X	X	X	X	X			X	X	X												3/1/23	
Install Fire Pro Main and components	Absolute Fire Pro	2/6/23			X	X	X			X	X	X	X	X			X	X	X	X	X			3/31/23	
Prime Paint	DTS Contracting	2/23/23				X	X			X	X	X	X	X			X	X	X	X	X				Where Available. Pull Ahead Task
Ceiling Grid Install	ACP	3/6/23															X	X	X	X	X			3/24/23	
Exterior Window Install		2/27/23								X	X	X	X	X			X	X	X	X	X			3/10/23	Where Applicable.
