



Farmington Public Schools

Gill Elementary

July 16, 2016



Project Overview



Removing asphalt at Power Upper
Elementary School

Project Overview




Underground plumbing for new office restrooms

Project Overview



Acoustical ceiling installation

Project Overview

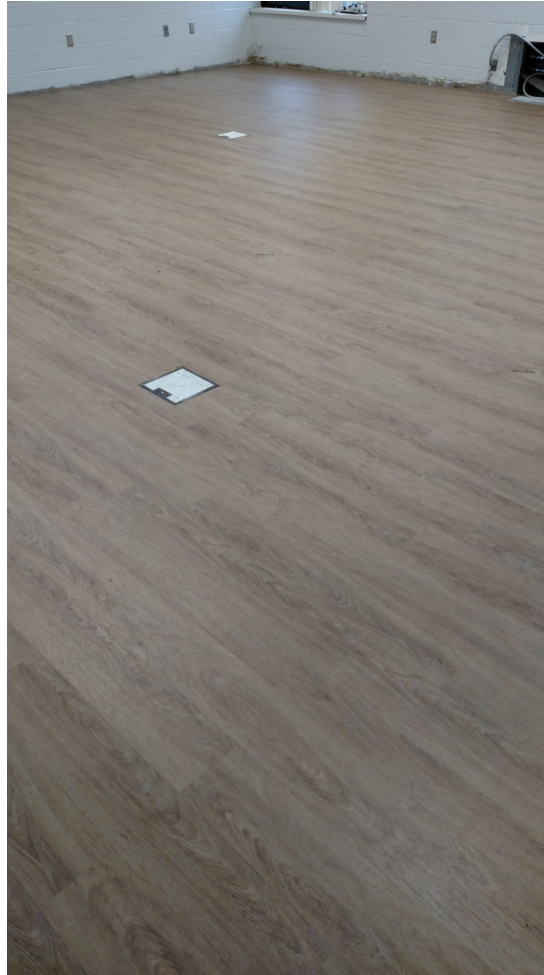

Flooring continues to be installed

Project Overview



Abatement complete

Two Week Look Ahead

Week of July 18

- **Finish & Sand drywall in corridors & classrooms**
- **Start framing in new office area**
- **Continue ceilings in media center**
- **Start floor tile in restrooms**
- **Reinforce trusses for RTUs**

Week of July 25

- **Replace asphalt parking**
- **Install RTUs**
- **Install existing millwork**
