



# Farmington Public Schools

Dunckel Middle School April 1, 2017



# Project Overview



Thin Brick starting to be installed in Media



# Project Overview




Materials for covering the skylights delivered to roof





# Project Overview

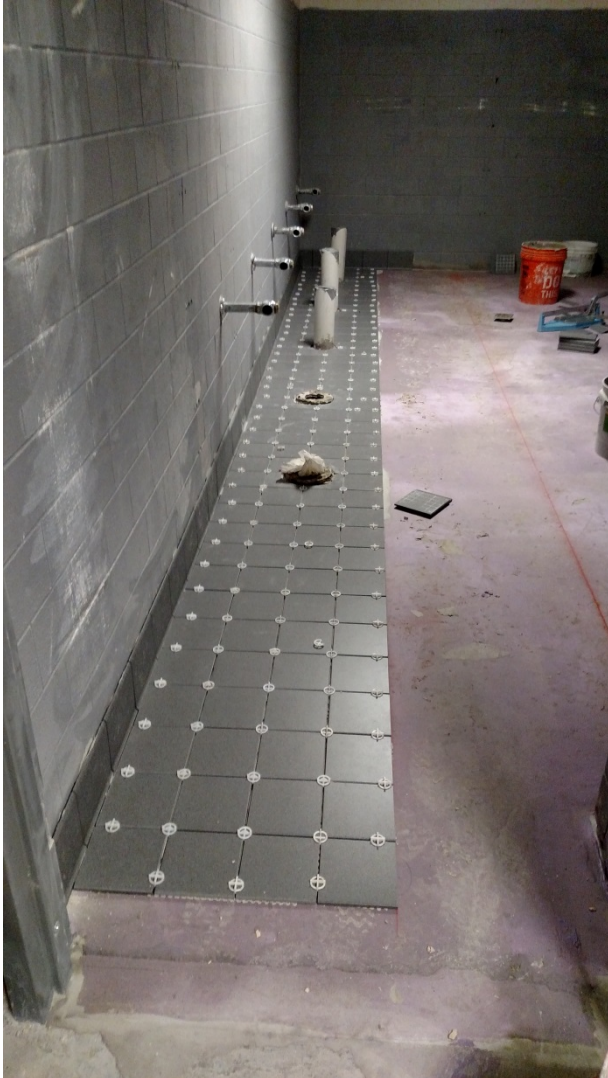

Hard Tile flooring in toilet rooms



# Project Overview



Classroom floors continue to be installed and covered



# Project Overview



Full height openings ready for new windows

## Two Week Look Ahead

### Week of 4/2/17

- Installing Ceiling Tile
- Finish Painting
- Start Roof Replacement

### Week of 4/9/17

- Start Pad for Greenhouse
- Install New Lay-in Light fixtures
- Start Carpet in Office Area
