



Farmington Public Schools

Dunckel Middle School April 22, 2017



Project Overview



Roofing Material Delivered & Start Installation

Project Overview




New White Boards Installed

Project Overview



Excavation on Greenhouse

Project Overview

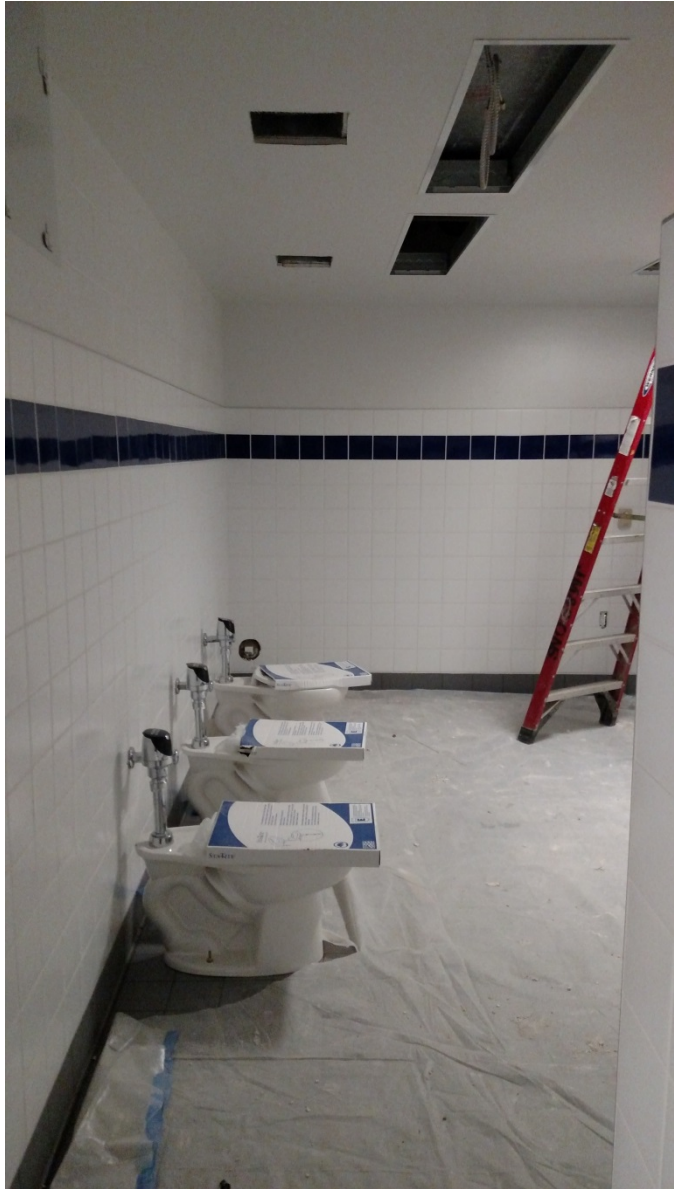

Toilet Rooms Tiled & Fixtures Installed

Project Overview



Window Treatment Complete

Two Week Look Ahead

Week of 4/23/17

- Installing Ceiling Tile
- Install Toilet Partitions
- Pour Pad For Greenhouse

Week of 4/30/17

- Start New Front Entrance
- Complete All Painting
- Start Blockwork For Greenhouse
