



Farmington Public Schools

Power Middle School

2017

July 17th thru July 28th




Project Overview




Main office vestibule coming along nicely. We met with Security Corp to coordinate all the in wall items needed for a secure and ADA approved entry.

Project Overview

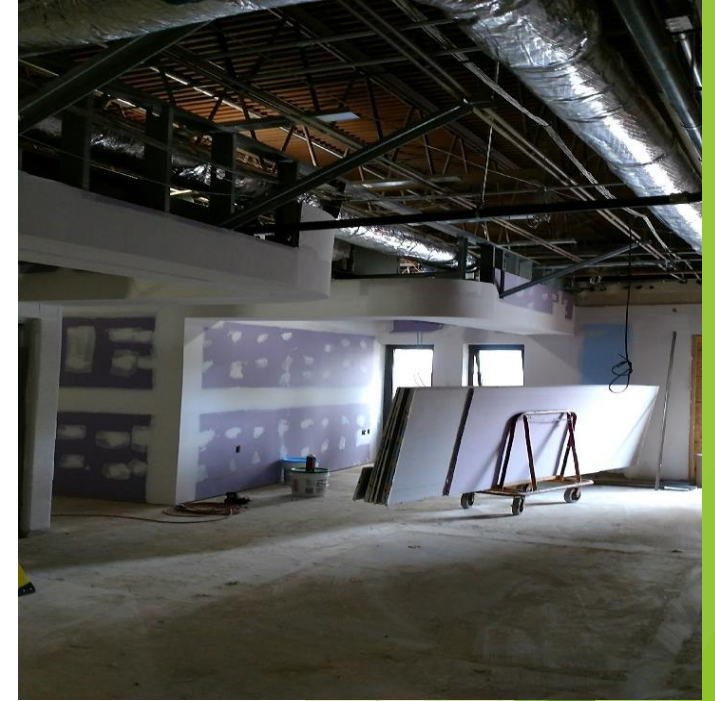



Main office door new frames toothed into existing masonry walls. New gyp walls and cmu wall constructed. Drywall radius soffits done. Drywall finishing underway.

Project Overview

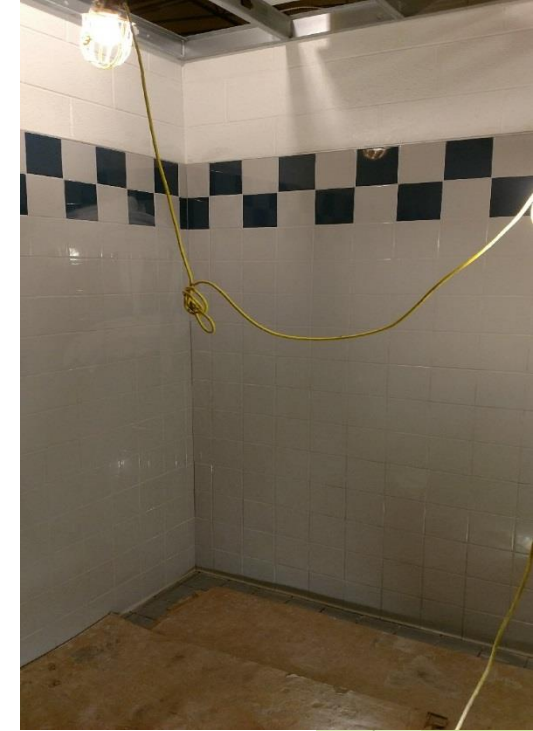

Here we have some ongoing finishes starting. Classroom flooring, gym floor sanding, and bathroom tile installation.

Project Overview

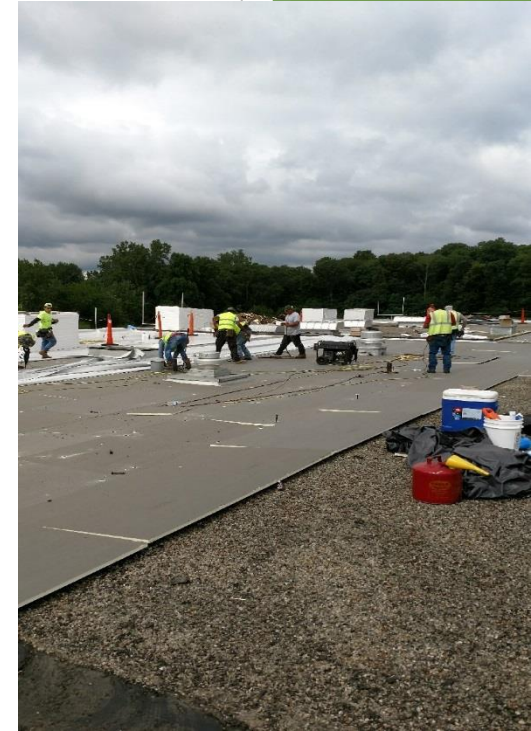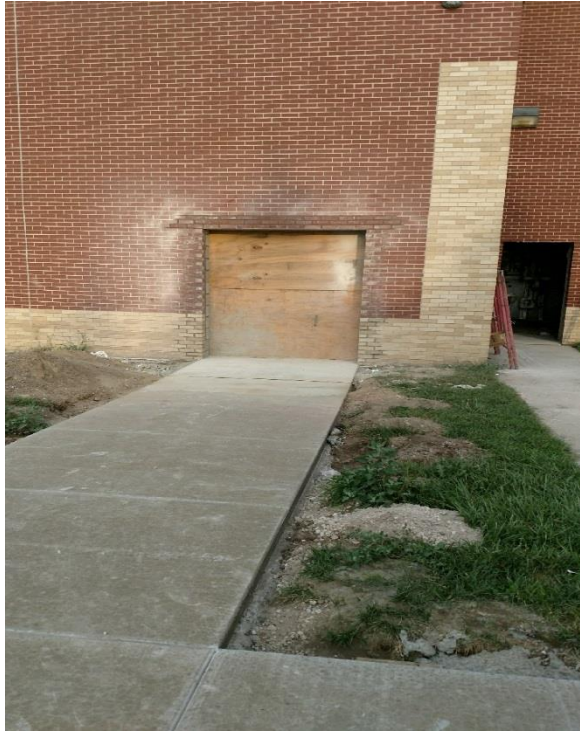

Lots of activity on the exterior of the building. New walk way on the east end with a new opening awaiting a new door. Panels going in on the south side and roofing underway.

Two Week Look Ahead

- - **Week of August 1st**

- **Ext Panels ongoing**
- **Roofing**
- **2nd floor duct and insulation**
- **Painting throughout**
- **Markerboard/Tackboard installation**
- **Bathroom Ceramic Tile/Grout**
- **Gym floor sanding**
- **LVT ongoing throughout**

Two Week Look Ahead

- **Week of August 7th**

- **Aluminum Frames/Glass/FRP Doors**
- **Roofing**
- **2nd floor Grid and Lights**
- **Painting throughout**
- **Bathroom Ceramic Tile/Grout**
- **Gym floor finishing**
- **LVT ongoing throughout**
- **Toilet Fixtures**
