




# Farmington Public Schools

## North Farmington High School

January 22, 2018



# Project Overview

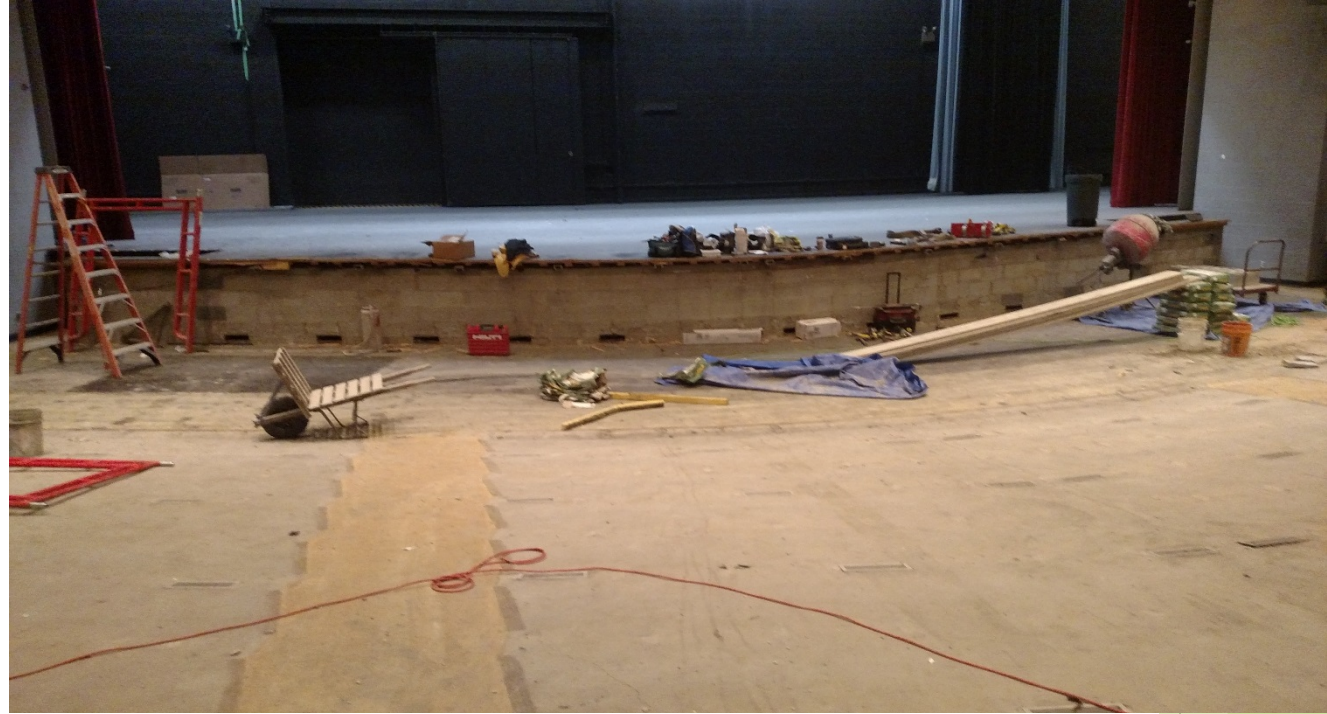

Demolition is underway in the auditorium, the seats have been removed and removal of the plaster ceiling is ongoing



# Project Overview



Demolition is also ongoing in the auditorium lobby.



# Project Overview



Demolition of the media center is complete and layout begins for the new main office area.



# Project Overview



Masonry for the new secure entrance, computer lab, and mechanical room are about 80% complete.



# Project Overview



Underground plumbing for the new office bathroom has been completed and new duct work for the main office is in place.



# Project Overview



Metal stud framing for the new layout is nearing completion.



# Two Week Look Ahead

## Main Office/Media center

- Completion of masonry walls.
- Rough electrical.
- Continue with mechanical installations.

## Auditorium

- Complete lobby demolition
- Complete all ground level demolition in auditorium.
- Erect scaffolding for overhead demolition of remaining ceiling, electrical, and mechanical.
- Complete demolition of control tower.
