



Farmington Public Schools



Power Middle School

2017

June 12th thru June 30th



Project Overview

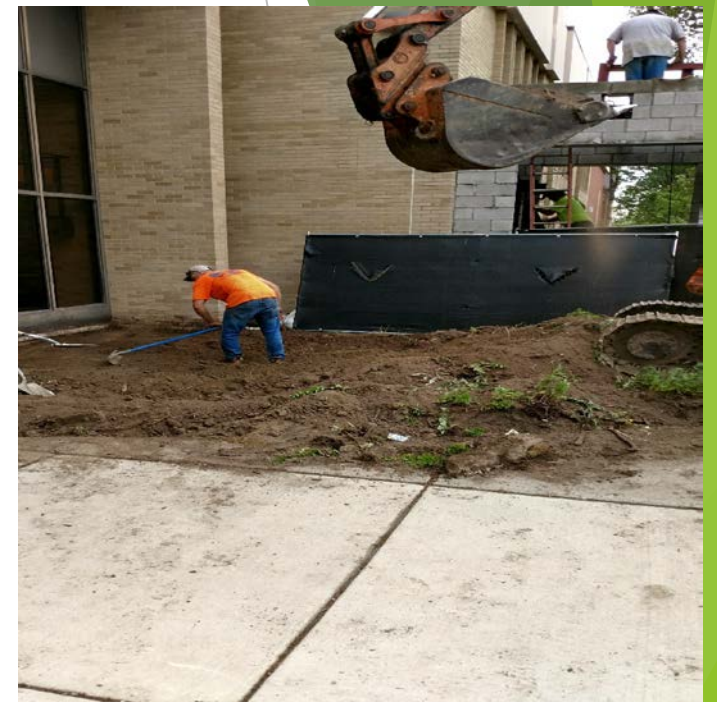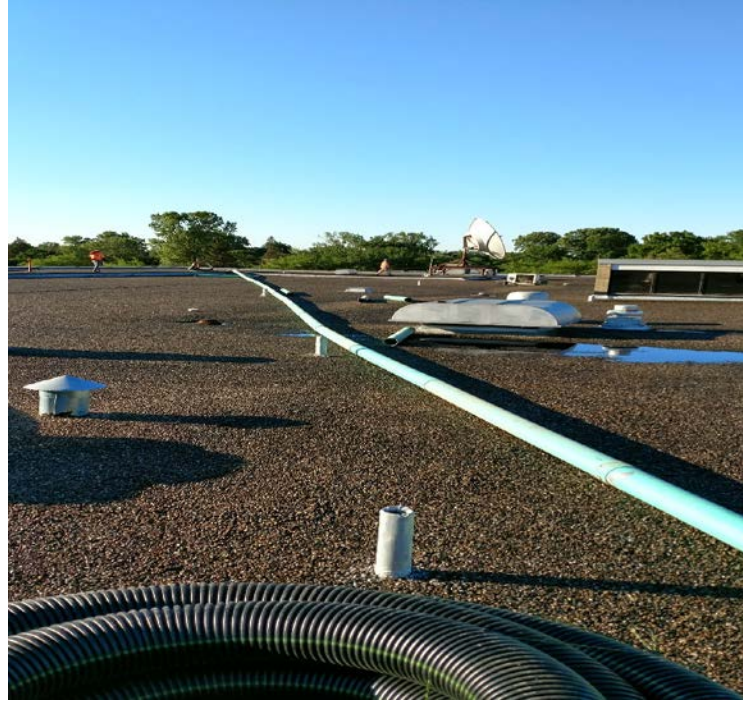

Over the past couple weeks a tremendous amount of demolition has been completed and is still underway. 2nd floor VCT and ceilings are 100% removed, roof gravel being extracted and hauled off site, and main entry vegetation and concrete removed.

Project Overview



Underground rough plumbing in the main office waiting on inspection, gymnasium bleachers gone, and new gym lights installed.

Project Overview



As you can see the new main entry vestibule is taking shape. We met with Security Corp to go over rough in wall items such as card reader, push pads, and other security items that may require in-wall pipe rough-ins.

Two Week Look Ahead

- **Week of June 26th**

- **Cont. MEP and Architectural demolition**
- **Swapping out of classroom ceiling pads**
- **Bleacher removal**
- **Vestibule masonry**
- **Orchestra Scaffold complete**

Week of July 3rd

- **Getting started on 2nd floor LVT prep**
- **2nd floor classroom painting and gym ceiling prep**
- **1st floor demo continues**
- **Main office masonry and carpentry partitions**
- **Vestibule and East entry concrete (weather permitting)**
